

French Quarter Infrastructure Improvement Project – Phase 2 *Status Update – December 14, 2018*

The City of New Orleans, Department of Public Works and Sewerage & Water Board began a full reconstruction project on Bourbon Street from St. Louis to Dumaine streets (500-800 blocks) on September 17, 2018. Work will occur sequentially from the 500 – 800 blocks, with ONLY one block fenced off at a time throughout construction. All businesses along this corridor will remain open and accessible throughout construction. The \$9.5 million cost-shared project, which is anticipated to run through June / July 2019, was designed by Mott McDonald, LLC and will be constructed by Hard Rock Construction, LLC. Project partners include Entergy Electric, Entergy Gas, Cox Communications and AT&T.

Attend our “Conversation on the Corner”

The next Phase 2 bi-weekly community status meeting will take place on Tuesday, December 18, at 10:30 a.m. at the Four Points Sheraton in the Board Room.

Upcoming Contractor Demobilization

No work will take place between December 24 & 25 and December 28-January 2, 2019 in advance of Christmas / New Year’s Eve / Sugar Bowl 2019. Currently, the schedule shows sidewalk work will be completed in the 500 block by December 23, weather permitting.

Traffic Status

Opening Tomorrow!!! The Toulouse intersection will reopen to vehicular traffic tomorrow.

500 Block Roadway – Open for Pedestrian Traffic Only

Crews are wrapping up removal of the sidewalks in preparation for the new bricks; all temporary access ramps to businesses have been installed. Both Entergy Electric and All Star Electric are continuing work in the 500 block on the removal/replacement of light poles.


Roadway Closure – 600 Block (Toulouse to St. Peter), Temporary Water Service Interruptions

Crews have installed the fence in the 600 block roadway to accommodate installation of new utilities. Crews are continuing work on the new waterline. **On Friday, December 14**, there will be a water line closure from 8 a.m. until 5 p.m. **Next Thursday, December 20**, the contractor will tie in the new waterline between 8 a.m. and 5 p.m. **NOTE:** Please expect temporary disruptions with water services during the above mentioned time frames.

Next Friday, December 21, the contractor will be completing individual service connections between 8 a.m. and 5 p.m.; businesses will be notified in advance.

UPDATED!!!! *Intersection Closure – St. Peter Street*

Minor work will be completed in the intersection of St. Peter and Bourbon streets that will NOT require a weeks-long closure as previously communicated. New concrete pavement will be installed in the intersection as part of the project; that activity will require an approximately week long closure once paving begins in January.

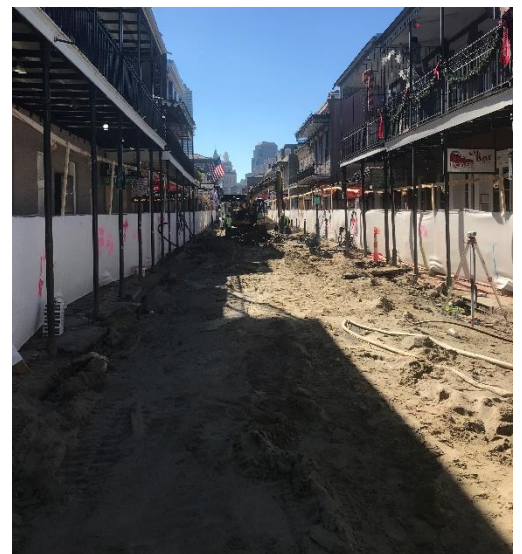

Entergy Electric & Gas

Entergy Gas will continue working at the intersection of St. Ann and Bourbon streets, and move into the 800 block. Entergy Electric will continue working in the 800 block. **There will be temporary street closures of Bourbon in the 800 block between 8:00 am and 5:00 pm seven days per week.** As usual Entergy will accommodate the public, businesses, and deliveries to the best of their ability.

Overall Project Sequence of Construction

Block	Tentative Schedule (Fence in place)	* Approximate Total Days Per Block (Including Sidewalks)
500 (St. Louis – Toulouse)	9/24/18 – 11/30/18	75 Days
600 (Toulouse – St. Peter)	12/03/18 – 1/27/19	75 Days
700 (St. Peter – St. Ann)	1/28/19 – 2/17/19, 3/7/19 - 4/22/19	75 Days
800 (St. Ann – Dumaine)	4/23/19 – 6/25/19	75 Days
Total Days *Once the contractor moves the fence to the next block, sidewalks in the previous block will be worked on simultaneously		250 Working Days Total (exclusive of weather / events days)

Mardi Gras Demobilization

The contractor will completely demobilize all labor and materials including fencing from the site and temporarily backfill any trenches by close of business on February 18, two weeks in advance of Mardi Gras, to minimize pedestrian and vehicular traffic disruption. The contractor will resume operations on March 7, 2019.

Demobilization for other Events / Holidays

The Contractor must contain equipment and materials within the block that is fenced off. No work will take place during the following event days or holidays: Christmas / New Year's Eve / Sugar Bowl (12/24 -12/25, 12/28-1/2/2019), French Quarter Fest (4/11-4/14), Jazz Fest (4/26-4/28 and 5/2-5/5).

Please Help Us Get the Message Out

We want to ensure that this information is reaching as many people as possible – French Quarter businesses, residents, hospitality workers, etc. Please help us to get the message out by sharing our weekly updates with your neighbors, staff; post in your breakrooms, on intranets, etc. If you wish to have anyone or any group added to our distribution list, please send an e-mail to roadwork@nola.gov. Thank you!

AT&T Service Outage Reporting Process

To ensure service restoration and proper credit, AT&T residential customers MUST report problems to 1-800-288-2020. Business customers MUST report problems to 1-877-438-0041. After reporting problems to AT&T, customers may also send e-mail to roadwork@nola.gov to help expedite the process.

Garbage Corrals

Garbage must be placed in appropriate corrals at the end of each intersecting block (St. Louis, Toulouse, etc.) between 4 a.m. to 8 a.m. and 4 p.m. to 8 p.m. Please refrain from leaving garbage cans on the Bourbon St. sidewalk as we are required to maintain pedestrian access.

How to Stay Informed

For regular updates on #RoadworkNOLA Projects, follow us on [Twitter](#), [Facebook](#) and [Instagram](#). You can also subscribe to our monthly newsletter by clicking [here](#) or visiting roadwork.nola.gov.

Questions about this project may be directed to via e-mail to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623).
