

French Quarter Infrastructure Improvement Project Status Update – June 12, 2017

The City of New Orleans, Department of Public Works, along with the Sewerage and Water Board of New Orleans, is currently implementing a **\$6M** reconstruction project which calls for removing and replacing existing water and drainage lines, repairing the sewer line, repaving the roadway in concrete, installing new sidewalks when necessary and installing American with Disabilities Act-compliant curb ramps at intersections.

Weekend Work Schedule

Construction crews will work regularly scheduled hours this Saturday (6/17). Crews will also be working on Sunday (6/18) beginning at 8 p.m. while construction crews line the sewer at the intersection of Bienville St.

Please note that all schedules are proposed and subject to weather delays and constructability issues.

“Conversation on the Corner”


The bi-weekly community status meetings will be held every other Thursday morning at 10 a.m. This week’s meeting will be held on **June 15 at 10 a.m.** on the corner of **Bienville and Bourbon** streets.

AT&T Service Outage Reporting Process

To ensure service restoration and proper credit, AT&T residential customers MUST report problems to 1-800-288-2020. Business customers MUST report problems to 1-877-438-0041. After reporting problems to AT&T, customers may also send e-mail to roadwork@nola.gov to expedite the process.

100 (Canal – Iberville) Anticipated Full Closure Construction Timeline: Apr. 24 – Aug. 5

- **Completed:** Installation of the new drainage siphon near Krystal is complete.
- Full block closure remains in effect.
- Installation of new 24 inch drain lines continues.
- **Ongoing Lane Reduction:** Expect one travel lane to be closed on Canal St. between Exchange Place and Bourbon St. in preparation for future pavement operations in the 100 block of Bourbon St.
- Removal and replacement of the Entergy duct bank continues.
- Entergy gas is removing the low pressure line on Canal St., **expect sidewalk disruptions.**
- Reminder to the adjacent businesses that the **sidewalk signage** should be taken into your venue each night.
- **Future road closure:** The intersection of Iberville and Bourbon St. is currently open but expected to close to through traffic when all the underground utilities are installed in the 100 block and crews are beginning to work in the 200 block of Bourbon St. **Expect this closure to begin June 14 and last for several weeks.** Note that during Essence Festival, this intersection will be re-opened to allow through traffic only.

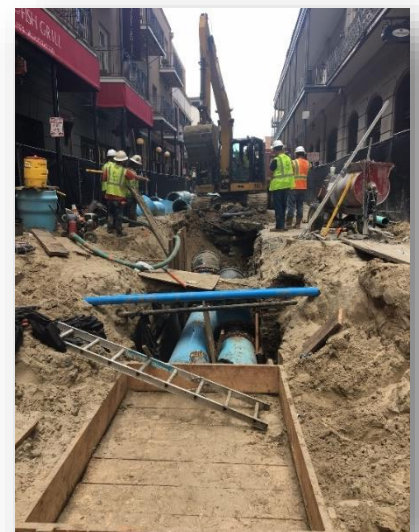

200 (Iberville – Bienville) Anticipated Full Closure Construction Timeline: Jul. 5 – Aug. 29

- Entergy Electric is currently installing new duct bank and conduits. Expect temporary lane closures during vault work.
- **Full closure is anticipated to begin following July 4 weekend and in advance of the 300 block being completed.**

300 (Bienville - Conti) Anticipated Full Closure Construction Timeline: May 15 – Aug. 18

- Construction crews are currently installing new water and drainage lines.
- Entergy Electric is nearly complete with duct bank and conduit tasks.
- Full block closure remains in effect.

400 (Conti – St. Louis) Anticipated Full Closure Construction Timeline: Jul. 5 – Aug. 29

- Ongoing exploratory work, expect parking lane closures
- **Full Closure will begin once the 100 block is reopened to traffic.**

500 (St. Louis - Toulouse) Anticipated Full Closure Construction Timeline: Sept. 5 – Oct. 26

- No work will occur until high Mississippi River conditions subside, which is anticipated around the early July timeframe.

600 (Toulouse - St. Peter) Anticipated Full Closure Construction Timeline: Nov. 1 – Dec. 15

No work will occur until high Mississippi River conditions subside, which is anticipated around the early July timeframe.

700 (St. Peter – St. Ann) Anticipated Full Closure Construction Timeline: Sept. 5 – Oct. 26

- No work will occur until high Mississippi River conditions subside, which is anticipated around the early July timeframe.

800 (St. Ann - Dumaine) Anticipated Full Closure Construction Timeline: Nov. 1 – Dec. 15

- No work will occur until high Mississippi River conditions subside, which is anticipated around the early July timeframe.

Questions about our French Quarter Infrastructure Improvement Project may be directed via e-mail to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623).

