

French Quarter Infrastructure Improvement Project – Phase 2

Status Update – September 28, 2018

The City of New Orleans, Department of Public Works and Sewerage & Water Board began a full reconstruction project on Bourbon Street from St. Louis to Dumaine streets (500-800 blocks) on September 17, 2018. Work will occur sequentially from the 500 – 800 blocks, with ONLY one block fenced off at a time throughout construction. All businesses along this corridor will remain open and accessible throughout construction. The \$9.5 million cost-shared project, which is anticipated to run through June 2019, was designed by Mott McDonald, LLC and will be constructed by Hard Rock Construction, LLC. Project partners include Entergy Electric, Entergy Gas, Cox Communications and AT&T.



Traffic Status

500 Block and St. Louis Intersection Remain Closed

Hard Rock Construction, LLC has completed installing the fence and temporary lighting in the 500 block of Bourbon Street. River bound traffic has been re-routed from the 500 block of Bourbon St. between St. Louis and Toulouse streets. The St. Louis intersection is also closed for approximately four more weeks so that crews can complete the installation of a syphon and other utilities. The 400 block of Bourbon and 700/800 blocks of St. Louis streets are closed to through traffic; flaggers will be on site at St. Louis and Royal and St. Louis and Dauphine while crews are working.

Entergy Electric & Gas

Entergy Gas has begun working in the 700 block from St. Peter to Orleans. Entergy Electric will continue construction in the 700 block of Bourbon St between St Peter and St. Ann. There will be no intersections closed; however, there will be temporary street closures of Bourbon in the 700 block between 8:00 am and 5:00 pm Monday through Friday. As usual Entergy will accommodate the public, businesses, and deliveries to the best of our ability.

NEW LOCATION - Attend our “Conversation on the Corner”

The next Phase 2 bi-weekly community status meeting will take place on Tuesday, October 9, at 10:30 a.m. at the Four Points Sheraton French Quarter, 541 Bourbon Street, New Orleans, LA 70130, Board Room.

Upcoming Week Work Plan

- ✓ **Saturday, Sept. 29:** Hard Rock personnel will be attending a safety training, so there will be no crews on site.

- ✓ **Sunday, Sept. 30 (Weather Permitting):** Crews will continue water line work, removal of the granite curb in the 500 block roadway, working on the syphon in the St. Louis intersection, and preparing for future lining of sewer house connections in the 800 block.
- ✓ **Monday, Oct. 1 – Friday, Oct. 5 (Weather Permitting):** Crews will continue water line work in the 500 block roadway and installation of the syphon in the St. Louis intersection.

Overall Project Sequence of Construction

Block	Tentative Schedule (Fence in place / Closed to Vehicular Traffic)	* Approximate Total Days Per Block (Including Sidewalks)
500 (St. Louis – Toulouse)	9/24/18 – 11/9/18	75 Days
600 (Toulouse – St. Peter)	11/10/18 – 1/21/19	75 Days
700 (St. Peter – St. Ann)	1/22/19 – 2/15/19, 3/7/19 - 4/6/19	75 Days
800 (St. Ann – Dumaine)	4/7/19 – 6/12/19	75 Days
Total Days *Once the contractor moves the fence to the next block, sidewalks in the previous block will be worked on simultaneously		250 Working Days Total (exclusive of weather / events days)

Please Help Us Get the Message Out

We want to ensure that this information is reaching as many people as possible – French Quarter businesses, residents, hospitality workers, etc. Please help us to get the message out by sharing our weekly updates with your neighbors, staff; post in your breakrooms, on intranets, etc. If you wish to have anyone or any group added to our distribution list, please send an e-mail to roadwork@nola.gov. Thank you!

AT&T Service Outage Reporting Process


To ensure service restoration and proper credit, AT&T residential customers MUST report problems to 1-800-288-2020. Business customers MUST report problems to 1-877-438-0041. After reporting problems to AT&T, customers may also send e-mail to roadwork@nola.gov to help expedite the process.

Garbage Corrals

Garbage must be placed in appropriate corrals at the end of each intersecting block (St. Louis, Toulouse, etc.) between 4 a.m. to 8 a.m. and 4 p.m. to 8 p.m. Please refrain from leaving garbage cans on the Bourbon St. sidewalk as we are required to maintain pedestrian access.

How to Stay Informed

For regular updates on #RoadWorkNOLA Projects, follow us on [Twitter](#), [Facebook](#) and [Instagram](#). You can also subscribe to our monthly newsletter by clicking [here](#) or visiting roadwork.nola.gov.

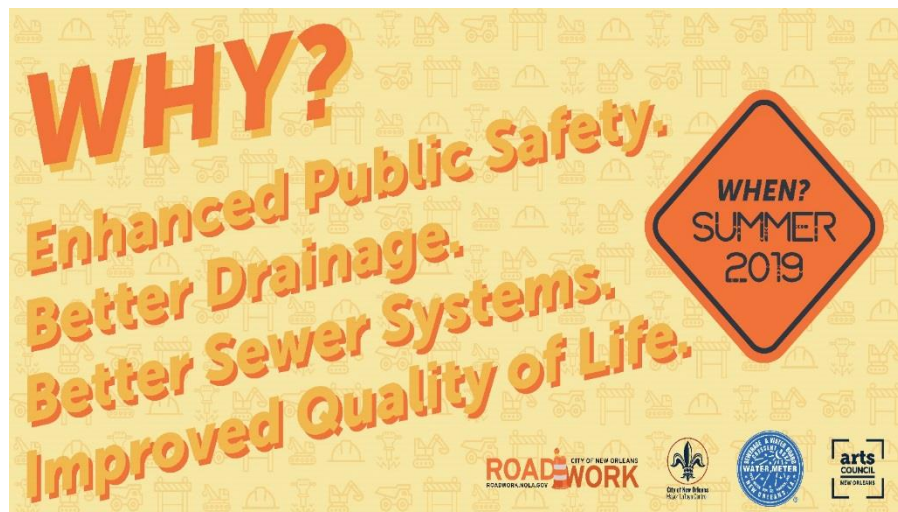

Questions about this project may be directed to via e-mail to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623).

