

French Quarter Infrastructure Improvement Project – Phase 2 *Status Update – January 4, 2019*

The City of New Orleans, Department of Public Works and Sewerage & Water Board began a full reconstruction project on Bourbon Street from St. Louis to Dumaine streets (500-800 blocks) on September 17, 2018. Work will occur sequentially from the 500 – 800 blocks, with ONLY one block fenced off at a time throughout construction. All businesses along this corridor will remain open and accessible throughout construction. The \$9.5 million cost-shared project, which is anticipated to run through June / July 2019, was designed by Mott McDonald, LLC and will be constructed by Hard Rock Construction, LLC. Project partners include Entergy Electric, Entergy Gas, Cox Communications and AT&T.

Attend our “Conversation on the Corner”

The next Phase 2 bi-weekly community status meeting will take place on Tuesday, January 8, at 10:30 a.m. at the Four Points Sheraton in the Board Room.

Mardi Gras Demobilization

The contractor will completely demobilize all labor and materials, including fencing, from the site and temporarily backfill any trenches by close of business on February 18, two weeks in advance of Mardi Gras, to minimize pedestrian and vehicular traffic disruption. The contractor will resume operations on March 7, 2019.


Traffic Status

500 Block Roadway – Open for Pedestrian Traffic Only

Crews have completed brick installation on the riverside sidewalk. Crews are scheduled to be completed with brick installation on the lakeside sidewalk by the end of next week (pictured). **NOTE:** The moveable bollard system will not be installed until the end of the project.

Roadway Closure – 600 Block (Toulouse to St. Peter)

Crews have completed work on the new waterline and are continuing work on the new drain line. Crews are in the process of completing house connections to tie in the new waterline to individual properties. **NOTE:** Expect intermittent sidewalk closures on Saturday (1/5) and Sunday (1/6); this activity could extend into early next week.

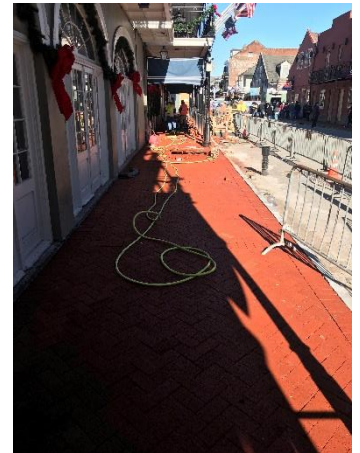

Intersection Closure – St. Peter Street

A water valve was damaged during installation of the water line in the 600 block. As a result, repair work must be completed in the St. Peter intersection that will require an approximately two week closure. The project team is in the process of determining when this work will occur.

Entergy Electric & Gas

Entergy Gas is continuing work at the intersection of St. Ann and Bourbon streets (expect daily closures), and will be moving into the 800 block. Entergy Electric will continue working in the 800 block. **There will be temporary street closures of Bourbon in the 800 block between 8:00 am and 5:00 pm seven days per week.** As usual, Entergy will accommodate the public, businesses, and deliveries to the best of their ability.

Overall Project Sequence of Construction

Block	Tentative Schedule (Fence in place)	* Approximate Total Days Per Block (Including Sidewalks)
500 (St. Louis – Toulouse)	9/24/18 – 11/30/18	75 Days
600 (Toulouse – St. Peter)	12/03/18 – 1/27/19	75 Days
700 (St. Peter – St. Ann)	1/28/19 – 2/17/19, 3/7/19 - 4/22/19	75 Days
800 (St. Ann – Dumaine)	4/23/19 – 6/25/19	75 Days
Total Days *Once the contractor moves the fence to the next block, sidewalks in the previous block will be worked on simultaneously		250 Working Days Total (exclusive of weather / events days)

Demobilization for other Events / Holidays

The Contractor must contain equipment and materials within the block that is fenced off. No work will take place during the following event days or holidays: French Quarter Fest (4/11-4/14), Jazz Fest (4/26-4/28 and 5/2-5/5).

Please Help Us Get the Message Out

We want to ensure that this information is reaching as many people as possible – French Quarter businesses, residents, hospitality workers, etc. Please help us to get the message out by sharing our weekly updates with your neighbors, staff; post in your breakrooms, on intranets, etc. If you wish to have anyone or any group added to our distribution list, please send an e-mail to roadwork@nola.gov. Thank you!

AT&T Service Outage Reporting Process

To ensure service restoration and proper credit, AT&T residential customers MUST report problems to 1-800-288-2020. Business customers MUST report problems to 1-877-438-0041. After reporting problems to AT&T, customers may also send e-mail to roadwork@nola.gov to help expedite the process.

Garbage Corrals

Garbage must be placed in appropriate corrals at the end of each intersecting block (St. Louis, Toulouse, etc.) between 4 a.m. to 8 a.m. and 4 p.m. to 8 p.m. Please refrain from leaving garbage cans on the Bourbon St. sidewalk as we are required to maintain pedestrian access.

How to Stay Informed

For regular updates on #RoadworkNOLA Projects, follow us on [Twitter](#), [Facebook](#) and [Instagram](#). You can also subscribe to our monthly newsletter by clicking [here](#) or visiting roadwork.nola.gov.

Questions about this project may be directed to via e-mail to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623).
