

French Quarter Infrastructure Improvement Project Status Update – November 14, 2017

The City of New Orleans, Department of Public Works, along with the Sewerage and Water Board of New Orleans, is currently implementing a **multi-million dollar** reconstruction project which calls for removing and replacing existing water and drainage lines, repairing the sewer line, repaving the roadway in concrete, installing new sidewalks, when necessary, and installing American with Disabilities Act-compliant curb ramps at intersections.

"Conversation on the Corner"

The bi-weekly community status meeting is held every other Thursday morning at 10 a.m. The next meeting will be held this **Thursday**, **November 16**th, **at 10 a.m.** on the corner of **Bienville and Bourbon** streets. **NOTE:** In the event of rain, we will meet at the PJ's in the Royal Sonesta.

Traffic Status

Intersection Closure at Conti St.

The intersection of Conti St. at Bourbon St. is currently closed. Conti St. is expected to re-open Thursday, Nov. 16, pending strength test results for the new concrete roadway. The closure is required to facilitate installation of underground utilities and permanent roadway restoration. Flaggers will be available at the intersections of Dauphine at Conti streets, and Royal at Conti streets to facilitate deliveries and access to parking garages.

Intersection Closure at Bienville St.

The intersection of Bienville at Bourbon St. will close after Conti St re-opens. The closure will last several weeks. The closure is required to facilitate installation of underground



utilities in the intersection and will begin once the Conti St. intersection re-opens. Flaggers will be available at the intersections of Dauphine at Bienville streets, and Royal at Bienville streets to facilitate deliveries and access to parking garages.

Business Signage

A number of businesses have printed and placed signage on the project safety fencing. The City is supportive of this effort; however, some of the signage has been defaced with stickers, graffiti, etc. Please plan to remove damaged signs and replace missing zip ties and brackets so the signage is affixed safely and legibly. Illegible and/or damaged signage will be removed on Thursday, Nov. 16.

100 (Canal - Iberville)

- Bollard installation is now scheduled for December.
- Please note the intersection of Iberville and Bourbon is currently a two-way stop. Both Bourbon and Iberville traffic are required to stop at the intersection.

200 (Iberville - Bienville) Anticipated Full Closure Construction Timeline: Jul. 5 - Mid-

December

- Full block closure remains in effect.
- Entergy Gas will complete all service connections by the end of the week.
- The remaining sewer house connections will be lined and/or replaced by the end of the week, completing the sewer work in this block.
- Crews will complete drainage in this block and extend the pipes through the Bienville intersection while it is closed.
- Plan to place garbage cans in appropriate corrals at the intersection of Iberville and Bienville streets. Garbage cans and carts may not be placed on the Bourbon St. sidewalk until construction is completed in the 200 block.



300 (Bienville - Conti) Anticipated Full Closure Construction Timeline: May 15 - Mid-December


- Full block closure remains in effect though pavement has been placed.
- New concrete will be poured in the two mid-block road closures this week. Pedestrians will be allowed to use the sidewalks at this time.
- Due to the Bienville closure and the Conti intersection still requiring utility and pavement work, this block will
 now be open to traffic in Mid-December. Pedestrians currently have access to both the street and the brick
 sidewalks.

400 (Conti - St. Louis) Anticipated Full Closure Construction Timeline: Sept. 7 - Dec. 2017

- Full block closure remains in effect.
- Entergy Gas is currently working in the 400 block.
- A new drainage siphon and all remaining drainage lines are scheduled to be completed this week.
- Roadway pavement restoration operations will begin in the next few weeks and be completed in December.

Work Schedule

Construction crews are now authorized to work from 6 a.m. to 6 p.m. Monday through Sunday, as weather permits. When possible, crews may work until 8 p.m.; however, high volumes of pedestrian activity make moving equipment more challenging late in the day.

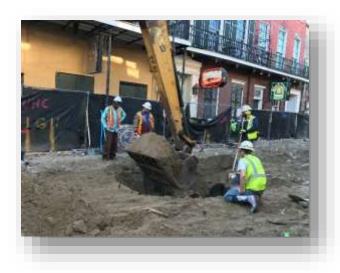

AT&T Service Outage Reporting Process

To ensure service restoration and proper credit, AT&T residential customers MUST report problems to 1-800-288-2020. Business customers MUST report problems to 1-877-438-0041. After reporting problems to AT&T, customers may also send e-mail to roadwork@nola.gov to expedite the process.

Garbage Corrals

Garbage must be **placed in appropriate corrals** at the end of each intersecting block (Iberville, Bienville and Conti) between 4 a.m. to 8 a.m. and 4 p.m. to 8 p.m. Please refrain from leaving garbage cans on the Bourbon St. sidewalk as we are required to maintain pedestrian access.

Questions about our French Quarter Infrastructure Improvement Project may be directed via e-mail to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623).

For regular updates on #RoadworkNOLA Projects, follow us on <u>Twitter</u>, <u>Facebook</u> and <u>Instagram</u>. You can also subscribe to our monthly newsletter by clicking <u>here</u> or visiting <u>roadwork.nola.gov</u>.
